GLAZING CHANNEL CHECKLIST

RIGHT-HAND CORNER SHOWER

(PANEL / DOOR / PANEL)

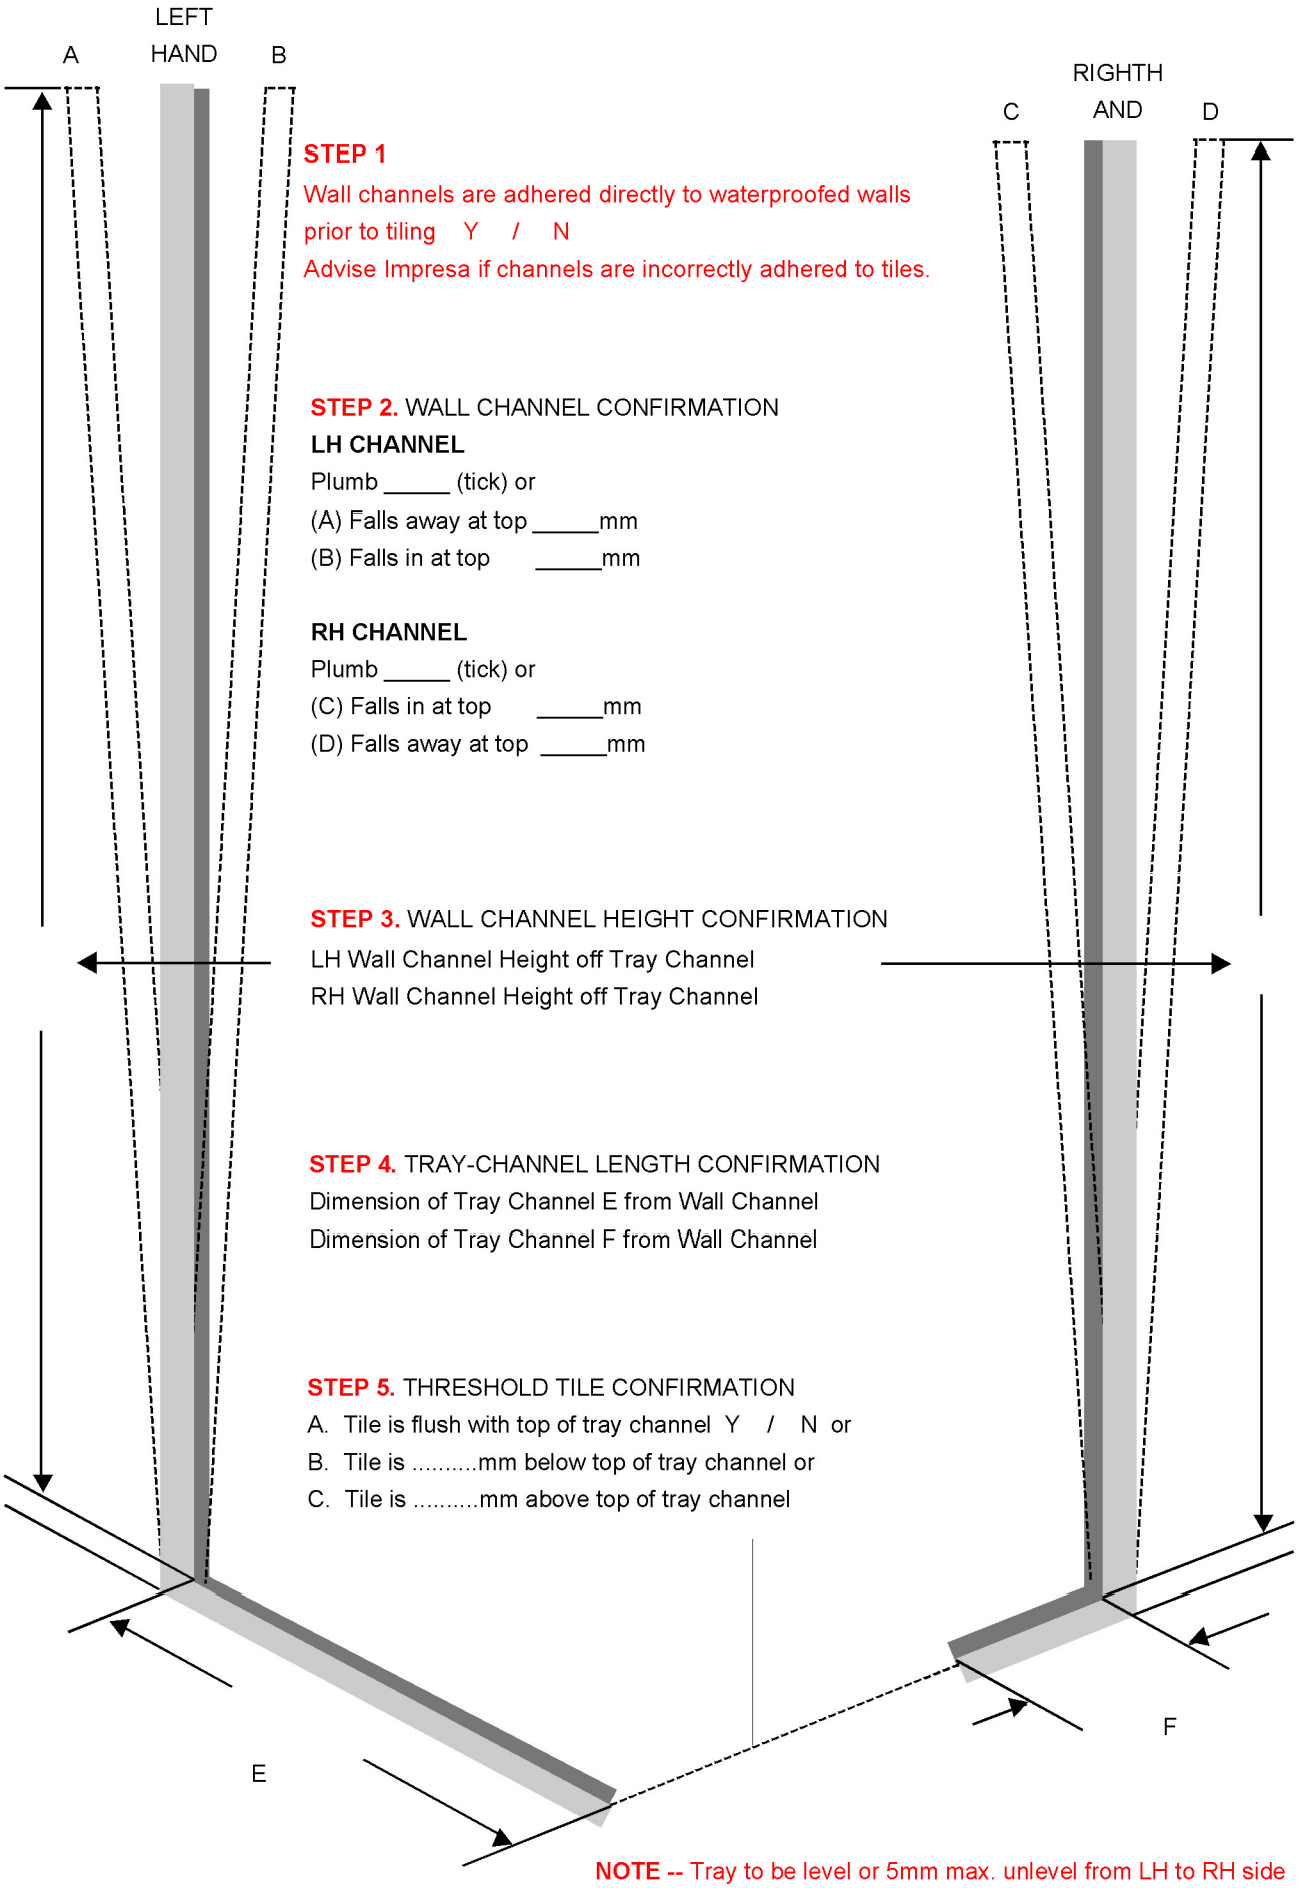

STEP 1

Wall channels are adhered directly to waterproofed walls prior to tiling Y / N

Advise Impresa if channels are incorrectly adhered to tiles.

STEP 2. WALL CHANNEL CONFIRMATION

LH CHANNEL

Plumb _____ (tick) or

(A) Falls away at top _____mm

(B) Falls in at top _____mm

RH CHANNEL

Plumb _____ (tick) or

(C) Falls in at top _____mm

(D) Falls away at top _____mm

STEP 3. WALL CHANNEL HEIGHT CONFIRMATION

LH Wall Channel Height off Tray Channel

RH Wall Channel Height off Tray Channel

STEP 4. TRAY-CHANNEL LENGTH CONFIRMATION

Dimension of Tray Channel E from Wall Channel

Dimension of Tray Channel F from Wall Channel

STEP 5. THRESHOLD TILE CONFIRMATION

A. Tile is flush with top of tray channel Y / N or

B. Tile is .....mm below top of tray channel or

C. Tile is .....mm above top of tray channel

NOTE -- Tray to be level or 5mm max. unlevel from LH to RH side
